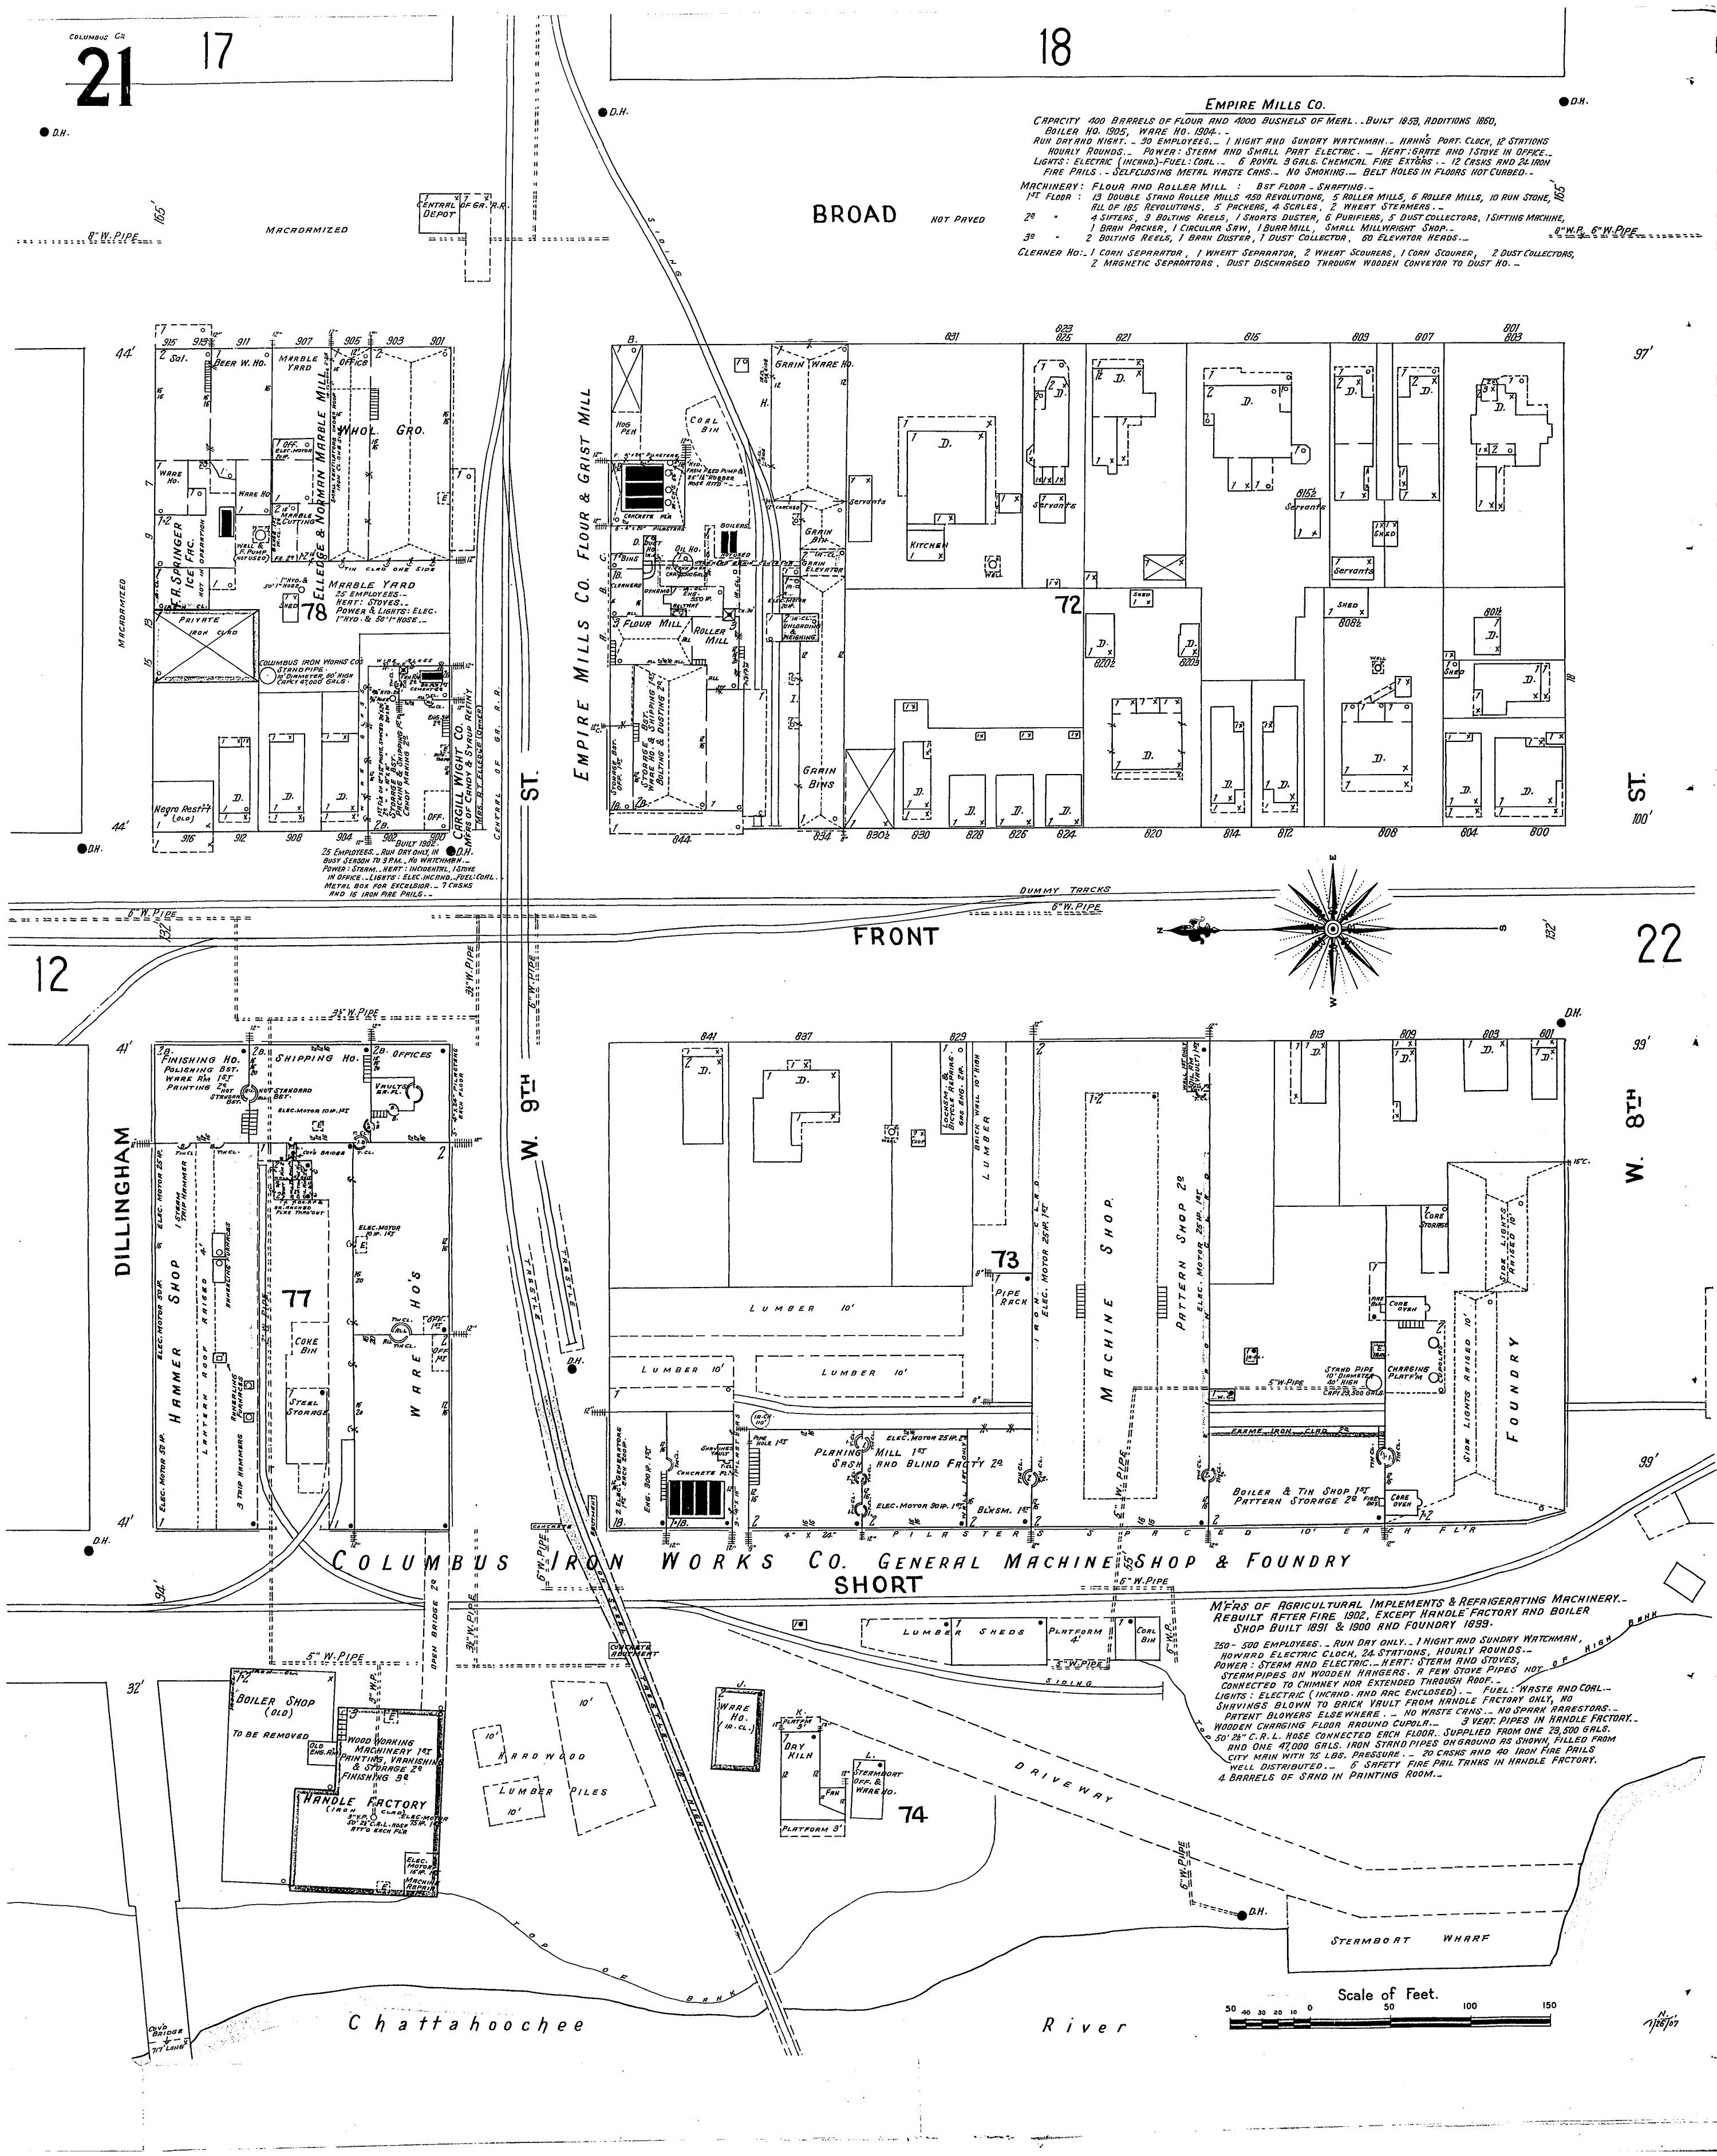
21
17
18
EMPIRE MILLS CO.
CAPACITY 400 BARRELS OF FLOUR AND 4000 BUSHELS OF MEAL..BUILT 1853, ADDITIONS 1860, BOILER HO. 1905, WARE HO. 1904.-
RUN DAY AND NIGHT.- 30 EMPLOYEES.- 1 NIGHT AND SUNDAY WATCHMAN.- HAHN'S PORT. CLOCK, 12 STATIONS HOURLY ROUNDS.- POWER: STEAM AND SMALL PART ELECTRIC.- HEAT: GRATE AND 1 STOVE IN OFFICE.-
LIGHTS: ELECTRIC (INCAND.)-FUEL: COAL.- 6 ROYAL 3 GALS. CHEMICAL FIRE EXT'G'RS.- 12 CASKS AND 24 IRON FIRE PAILS.- SELFCLOSING METAL WASTE CANS.- NO SMOKING.- BELT HOLES IN FLOORS NOT CURBED.-
MACHINERY: FLOUR AND ROLLER MILL : BST FLOOR - SHAFTING.-
1ST FLOOR : 13 DOUBLE STAND ROLLER MILLS 450 REVOLUTIONS, 5 ROLLER MILLS, 6 ROLLER MILLS, 10 RUN STONE, ALL OF 185 REVOLUTIONS, 5 PACKERS, 4 SCALES, 2 WHEAT STEAMERS.-
2D " 4 SIFTERS, 9 BOLTING REELS, 1 SHORTS DUSTER, 6 PURIFIERS, 5 DUST COLLECTORS, 1 SIFTING MACHINE, 1 BRAN PACKER, 1 CIRCULAR SAW, 1 BURR MILL, SMALL MILLWRIGHT SHOP.-
3D " 2 BOLTING REELS, 1 BRAN DUSTER, 1 DUST COLLECTOR, 60 ELEVATOR HEADS.-
CLEANER HO:- 1 CORN SEPARATOR, 1 WHEAT SEPARATOR, 2 WHEAT SCOURERS, 1 CORN SCOURER, 2 DUST COLLECTORS, 2 MAGNETIC SEPARATORS. DUST DISCHARGED THROUGH WOODEN CONVEYOR TO DUST HO.-
BROAD
NOT PAVED
MACADAMIZED
8" W. PIPE
CENTRAL OF GA. R.R. DEPOT
EMPIRE MILLS CO. FLOUR & GRIST MILL
ELLEDGE & NORMAN MARBLE MILL
MARBLE YARD
WHOL. GRO.
BEER W. HO.
F.R. SPRINGER ICE FAC.
CARGILL WIGHT CO. CANDY & SYRUP REFINY
COLUMBUS IRON WORKS CO. STANDPIPE
Negro Rest't (OLD)
GRAIN WARE HO.
GRAIN ELEVATOR
GRAIN BINS
FLOUR MILL
ROLLER MILL
72
78
W. 9TH ST.
W. 8TH ST.
FRONT
DUMMY TRACKS
6" W. PIPE
12
22
DILLINGHAM
FINISHING HO.
SHIPPING HO.
OFFICES
HAMMER SHOP
WARE HO'S
COKE BIN
STEEL STORAGE
77
73
LUMBER
MACHINE SHOP
PATTERN SHOP 2D
FOUNDRY
PLANING MILL 1ST SASH AND BLIND FACT'Y 2D
BLKSM. 1ST
BOILER & TIN SHOP 1ST PATTERN STORAGE 2D
CORE OVEN
COLUMBUS IRON WORKS CO. GENERAL MACHINE SHOP & FOUNDRY
SHORT
M'F'RS OF AGRICULTURAL IMPLEMENTS & REFRIGERATING MACHINERY.- REBUILT AFTER FIRE 1902, EXCEPT HANDLE FACTORY AND BOILER SHOP BUILT 1891 & 1900 AND FOUNDRY 1899.
250-500 EMPLOYEES.- RUN DAY ONLY.- 1 NIGHT AND SUNDAY WATCHMAN, HOWARD ELECTRIC CLOCK, 24 STATIONS, HOURLY ROUNDS.-
POWER: STEAM AND ELECTRIC.- HEAT: STEAM AND STOVES, STEAMPIPES ON WOODEN HANGERS. A FEW STOVE PIPES NOT CONNECTED TO CHIMNEY NOR EXTENDED THROUGH ROOF.-
LIGHTS: ELECTRIC (INCAND. AND ARC ENCLOSED).- FUEL: WASTE AND COAL.- SHAVINGS BLOWN TO BRICK VAULT FROM HANDLE FACTORY ONLY, NO PATENT BLOWERS ELSEWHERE.- NO WASTE CANS.- NO SPARK ARRESTORS.-
WOODEN CHARGING FLOOR AROUND CUPOLA.- 3 VERT. PIPES IN HANDLE FACTORY.-
50' 2½" C.R.L. HOSE CONNECTED EACH FLOOR.. SUPPLIED FROM ONE 23,500 GALS. AND ONE 47,000 GALS. IRON STAND PIPES ON GROUND AS SHOWN, FILLED FROM CITY MAIN WITH 75 LBS. PRESSURE.- 20 CASKS AND 40 IRON FIRE PAILS WELL DISTRIBUTED.- 6 SAFETY FIRE PAIL TANKS IN HANDLE FACTORY.
4 BARRELS OF SAND IN PAINTING ROOM..
TOP OF HIGH BANK
BOILER SHOP (OLD) TO BE REMOVED
WOOD WORKING MACHINERY 1ST PAINTING, VARNISHING & STORAGE 2D FINISHING 3D
HANDLE FACTORY
LUMBER SHEDS
PLATFORM
HARDWOOD LUMBER PILES
DRY KILN
STEAMBOAT OFF. & WARE HO.
74
DRIVEWAY
SIDING
STEAMBOAT WHARF
TOP OF BANK
Chattahoochee River
Scale of Feet.
50 40 30 20 10 0 50 100 150
