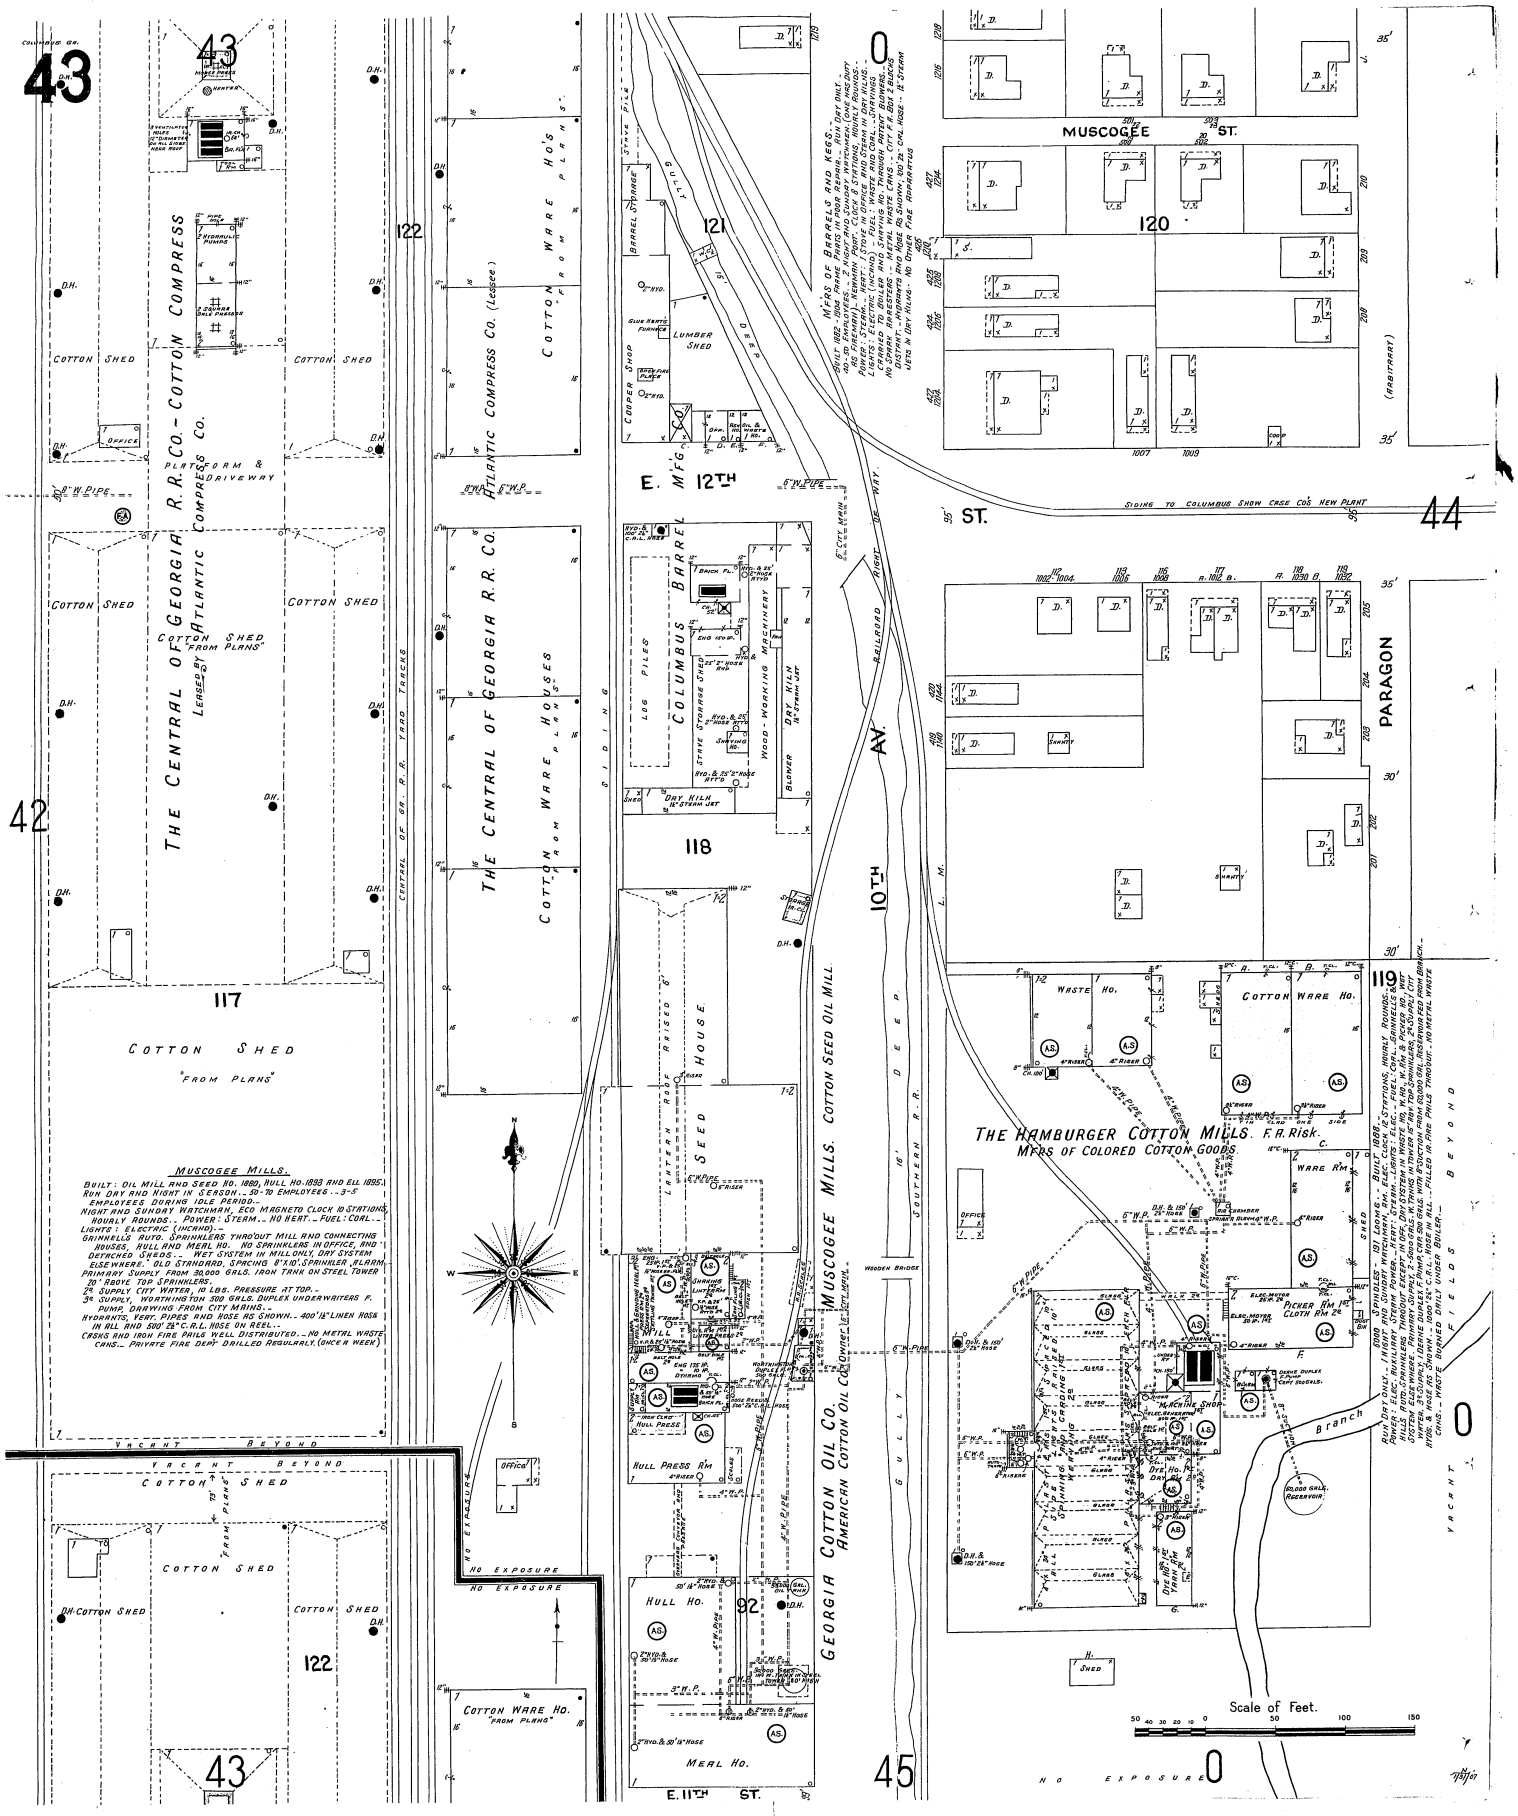
THE CENTRAL OF GEORGIA R.R. CO. - COTTON COMPRESS
ATLANTIC COMPRESS CO.
LEASED BY ATLANTIC COMPRESS CO.
COTTON SHED
PLATFORM & DRIVEWAY
OFFICE
COTTON SHED "FROM PLANS"
COTTON WARE HO'S
ATLANTIC COMPRESS CO. (Lessee)
THE CENTRAL OF GEORGIA R.R. CO.
COTTON WARE HOUSES
CENTRAL OF GEO. R.R. YARD TRACKS
SIDING
COLUMBUS BARREL MFG CO.
LOG PILES
STAVE STORAGE SHED
WOOD-WORKING MACHINERY
DRY KILN
BLOWER
LUMBER SHED
COOPER SHOP
BARREL STORAGE
GULLY
E. 12TH
E. 11TH ST.
MUSCOGEE ST.
PARAGON
SIDING TO COLUMBUS SHOW CASE CO'S NEW PLANT
MFRS OF BARRELS AND KEGS.
BUILT 1892 - 1894 FRAME, PARTS IN GOOD REPAIR. - RUN DAY AND NIGHT IN SEASON. - 30-40 EMPLOYEES. - 3-5 EMPLOYED DURING IDLE PERIOD. - NIGHT AND SUNDAY WATCHMAN AS FIREMAN. - NEWMAN PORT. CLOCK & STATIONS, HOURLY ROUNDS. - POWER: STEAM. - NO HEAT. - FUEL: COAL. - LIGHTS: STEAM, INCAND. - ELECTRIC IN OFFICE AND STEAM IN DRY KILNS. - PROTECTED BY 2" HYD. & 50' 2½" RUBBER HOSE. - NO SPRINKLERS. - CARRIED TO BOILER AND SHAVINGS NO. THROUGH PATENT BLOWERS. - WATER: CITY. - NO PRIVATE FIRE DEPT. - NEAREST ENGINE HOUSE 1 BLK. DISTANT. - HYDRANTS AND HOSE AS SHOWN. (100) 2½" CAL. HOSE - 16 STORZ VLVS IN DRY KILNS. - NO OTHER FIRE APPARATUS
COTTON SEED OIL MILL
GEORGIA COTTON OIL CO.
AMERICAN COTTON OIL CO. OWNER: LEASE MILL.
MUSCOGEE MILLS.
MUSCOGEE MILLS.
BUILT - OIL MILL AND SEED HO. 1880, HULL HO. 1893 AND ELL 1895. - RUN DAY AND NIGHT IN SEASON. - 30-40 EMPLOYEES. - 3-5 EMPLOYED DURING IDLE PERIOD. - NIGHT AND SUNDAY WATCHMAN, ECO MAGNETO CLOCK 10 STATIONS, HOURLY ROUNDS. - POWER: STEAM. - NO HEAT. - FUEL: COAL. - LIGHTS: ELECTRIC (INCAND). - SPRINKLERS AUTO. SPRINKLERS THRO'OUT MILL AND CONNECTING HOUSES, HULL AND MEAL HO. NO SPRINKLERS IN OFFICE, AND DETACHED SHEDS. - WET SYSTEM IN MILL ONLY, DRY SYSTEM ELSEWHERE. - OLD STANDARD, SPACING 8'X10', SPRINKLER, PLAIN. PRIMARY SUPPLY FROM 30,000 GALS. IRON TANK ON STEEL TOWER 20' ABOVE TOP SPRINKLERS. 2ND SUPPLY CITY WATER, 10 LBS. PRESSURE AT TOP. - 3RD SUPPLY, WORTHINGTON 500 GALS. DUPLEX UNDERWRITERS F. PUMP, DRAWING FROM CITY MAINS. - HYDRANTS, FEET, PIPES AND HOSE AS SHOWN. - 400' 1½" LINEN HOSE IN ALL AND 500' 2½" C.R.L. HOSE ON REEL. - CASKS AND IRON FIRE PAILS WELL DISTRIBUTED. - NO METAL WASTE CANS. - PRIVATE FIRE DEPT. DRILLED REGULARLY. (ONCE A WEEK)
SEED HOUSE
HULL PRESS RM
HULL HO.
MEAL HO.
COTTON WARE HO. "FROM PLANS"
NO EXPOSURE
VACANT BEYOND
THE HAMBURGER COTTON MILLS. F.R. Risk.
MFRS OF COLORED COTTON GOODS
WASTE HO.
COTTON WARE HO.
WARE RM
PICKER RM
CLOTH RM
MACHINE SHOP
DYE HO.
YARN RM
OFFICE
SHED
RUN DAY ONLY. - NIGHT AND SUNDAY WATCHMAN, RM. ELEC. CLOCK & STATIONS, HOURLY ROUNDS. - 1891 LOOMS. - BUILT 1888. - 6000 SPINDLES. - 191 LOOMS. - 1-ELEC. ELEVATOR. - 1-ELEC. HOIST. - POWER: ELEC. - LIGHTS: ELEC. - WATER: CITY. - HILLS AUTO. SPRINKLERS THROUT EXCEPT IN OFF. DRY SYSTEM IN WASTE HO. WET SYSTEM ELSEWHERE. PRIMARY SUPPLY 1-300 BBLS. IN TOWER 8' BELOW TOP SPRINKLERS. 2ND SUPPLY CITY WATER. - 3RD SUPPLY, WORTHINGTON DUPLEX 500 GALS. - 4TH SUPPLY, 30,000 GALS. IRON TANK ON STEEL TOWER 20' ABOVE TOP SPRINKLERS. - HYDS. & HOSE AS SHOWN. - 500' 1½" C.R.L. HOSE IN HILL. - FILLED IN DRY PHILS THROUGH. - NO METAL WASTE CANS. - WASTE BURNED DAILY UNDER BOILER. -
BOILER GALS. RESERVOIR
Branch
VACANT BEYOND
Scale of Feet.
50 40 30 20 10 0 50 100 150
